

03-0976
Patel et al.
Test Schedule Estimator for Legacy Builds

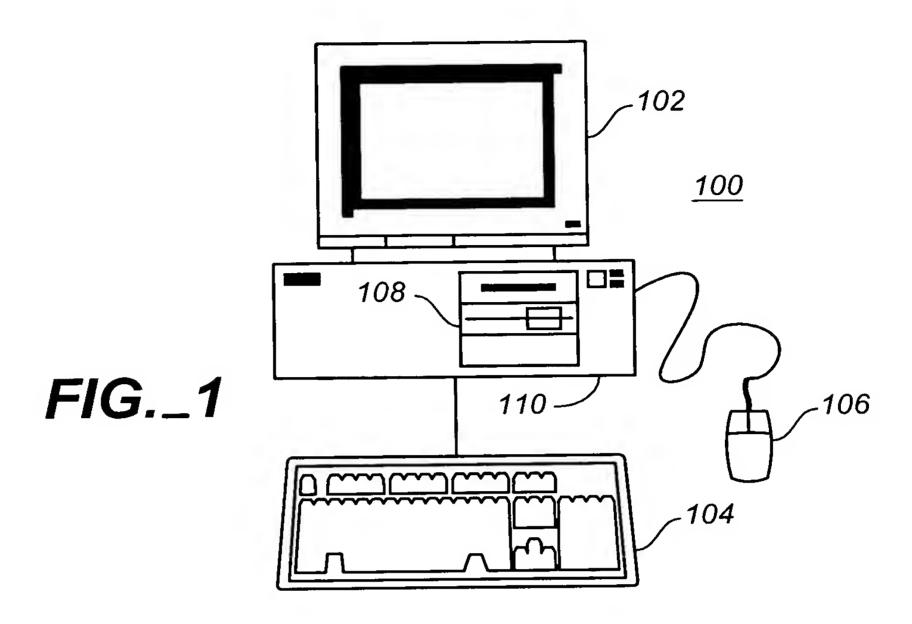

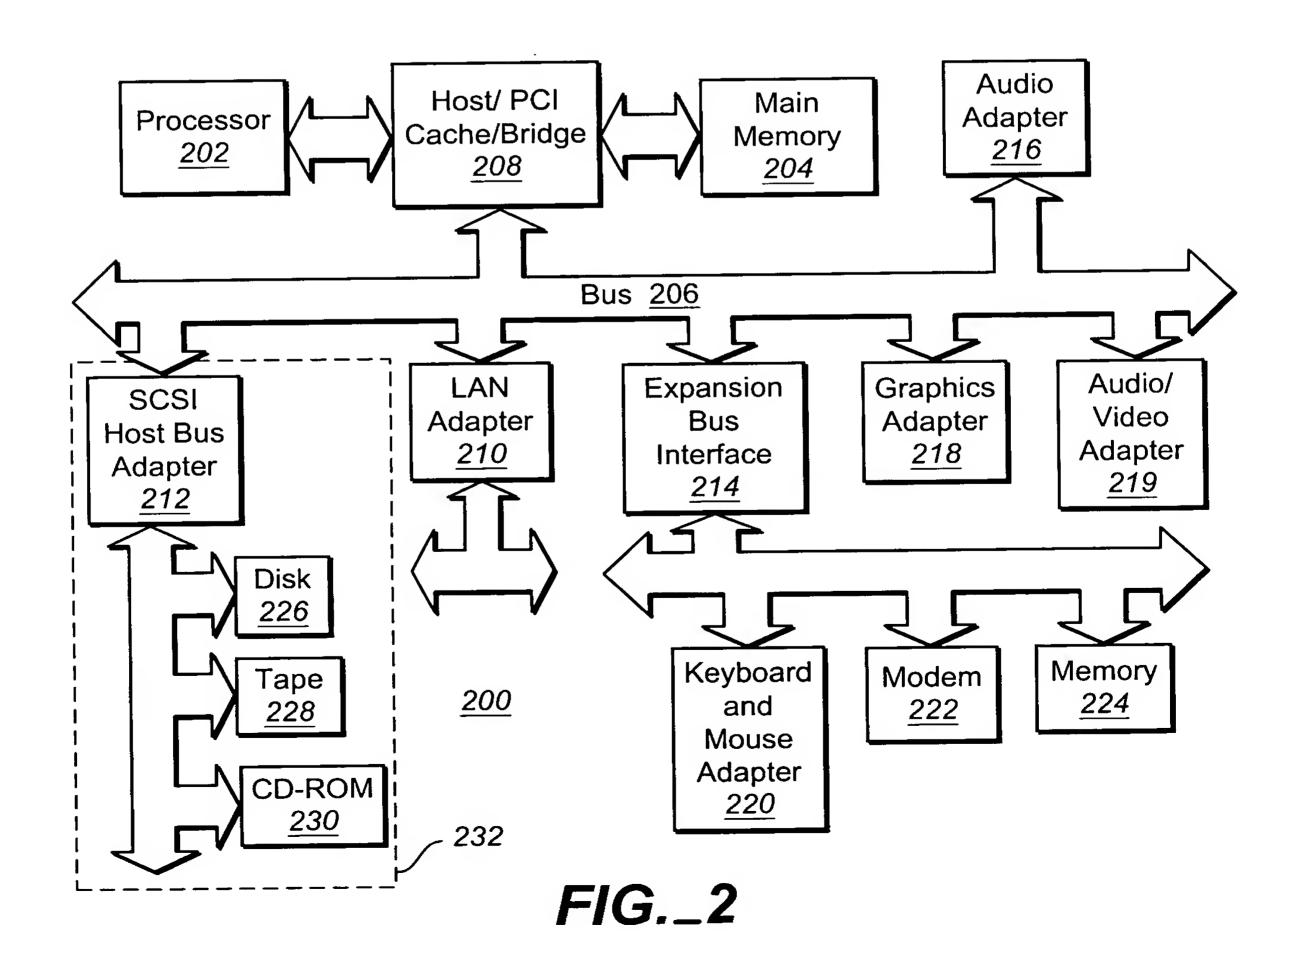

03-0976
Patel et al.
Test Schedule Estimator for Legacy Builds

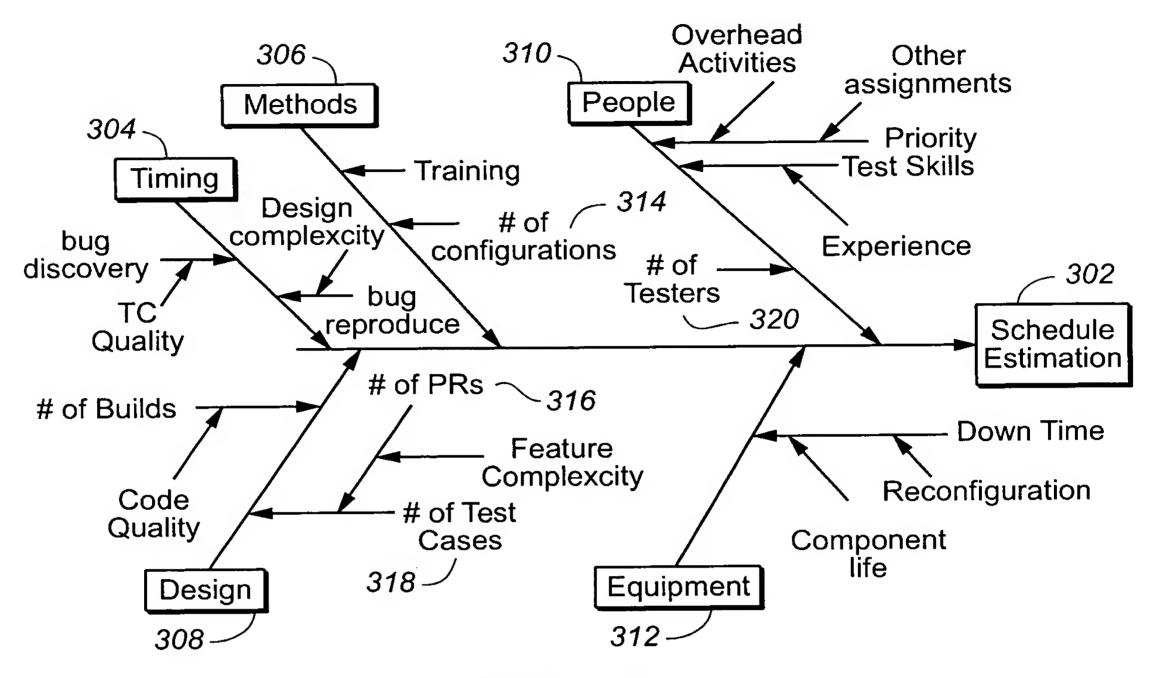


FIG._3

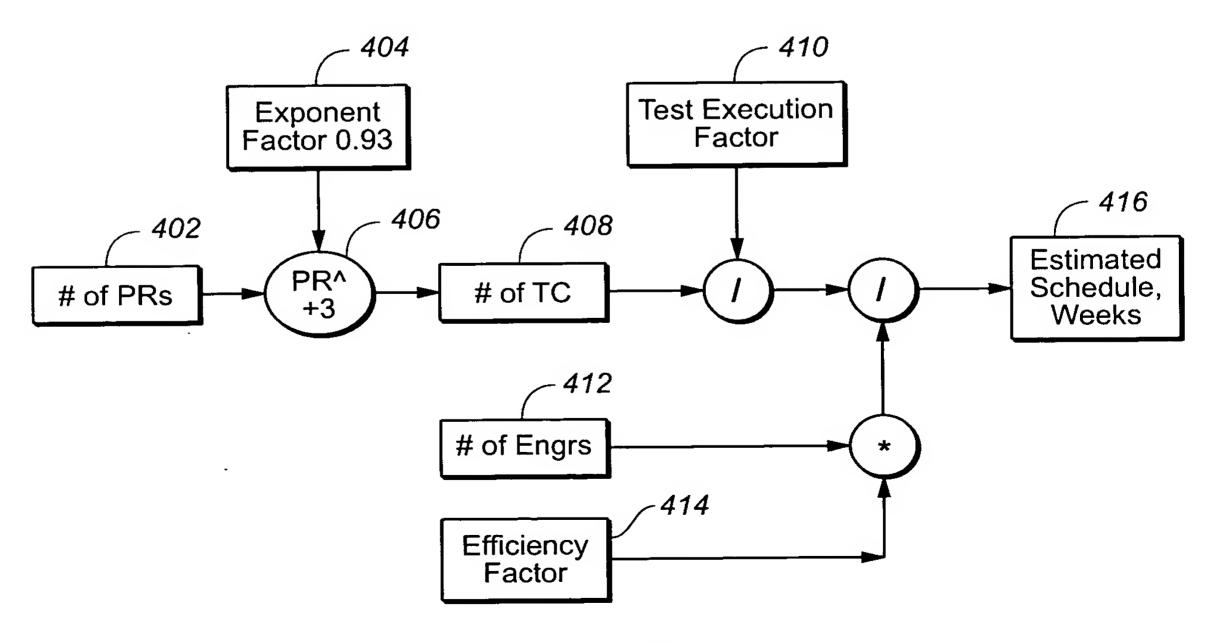


FIG._4

03-0976
Patel et al.
Test Schedule Estimator for Legacy Builds

10 4	3/5							
test cases/ tester-wk	ion Factors	0.69	0.57	1.28	95.0	1.59	4.83	4.15
test cases/ Cal-Wk	Test Execut	0.76	0.7	1.59	69.0	1.99	5.23	4.61
Eng wks (Calendar)		32.22	33.08	30	28.27	15.25	8.21	11.11
test wks (Calendar)		29	27	24	23	12.2	7.58	10
FTE Eng		6	10	11	12	8	3	1.8
TC/Eng		22	19	38	16	24	40	46
Unique TC		199	188	421	190	194	119	83
SYMsm 7/4.x/8/5.x		I Overall Viking 1	Overall Viking 2	2 Overall Viking 3	Overall Mojave 1-Tier 1	2 Overall Sonoran 1 (8.0/5.0)	3 Overall Mojave 2-Solaris 8/W2K	Sonoran 1M Regression (120 PRs)
		G1	G1	G2	G1	G2	G3	63
	Unique TC/Eng FTE Eng (Calendar) (Calendar) Cal-Wk	Unique TC/Eng FTE Eng (Calendar) (Calendar) Cal-Wk Test cases/	SYMsm 7/4.x/8/5.x Unique TC/Eng TC/Eng FTE Eng (Calendar) (Calendar) (Calendar) Calendar) (Calendar) Calendar Test Execution Calendar Overall Viking 1 199 22 9 29 32.22 0.76	SYMsm 7/4.x/8/5.x Unique TC/Eng TC TC/Eng (Calendar) FTE Eng (Calendar) FTE Eng (Calendar) test wks (Calendar) test cases/Cal-Wk Overall Viking 1 199 22 9 29 32.22 0.76 Overall Viking 2 188 19 10 27 33.08 0.7	SYMsm 7/4.x/8/5.x Unique TC/Eng TC/Eng FTE Eng (Calendar) (Calendar) FTE Eng (Calendar) test cases/Calendar Overall Viking 2 199 22 9 29 32.22 0.76 Overall Viking 3 421 38 11 24 30 1.59	SYMsm 7/4.x/8/5.x Unique TC/Eng	SYMsm 7/4.x/8/5.x Unique TC/Eng TC TC/Eng TC FTE Eng (Calendar) (Cale	SYMsm 7/4.x/8/5.x Unique TC/Eng TC TC/Eng TC FTE Eng (Calendar) (Cale

F/G._5


03-0976
Patel et al.
Test Schedule Estimator for Legacy Builds

Schedule in Weeks

Schedule III Wooks								
PRs	Aggressive	70% Confidence	High Confidence					
1	0.42	0.51	0.62					
2	0.52	0.62	0.76					
3	0.61	0.73	0.90					
4	0.70	0.84	1.03					
5	0.79	0.95	1.16					
10	1.22	1.46	1.78					
15	1.64	1.96	2.39					
20	2.04	2.44	2.98					
25	2.44	2.92	3.56					
30	2.83	3.38	4.13					
35	3.22	3.85	4.69					
40	3.60	4.31	5.25					
45	3.98	4.76	5.81					
50	4.36	5.21	6.36					
55	4.73	5.66	6.90					
60	5.10	6.10	7.44					
65	5.47	6.55	7.98					
70	5.84	6.99	8.52					
75	6.21	7.42	9.05					
80	6.57	7.86	9.59					
85	6.93	8.29	10.11					
90	7.30	8.72	10.64					
95	7.66	9.16	11.17					
100	8.01	9.58	11.69					
105	8.37	10.01	12.21					
110	8.73	10.44	12.73					
115	9.08	10.86	13.25					
120	9.44	11.28	13.76					
125	9.79	11.71	14.28					

FIG._6

03-0976
Patel et al.
Test Schedule Estimator for Legacy Builds

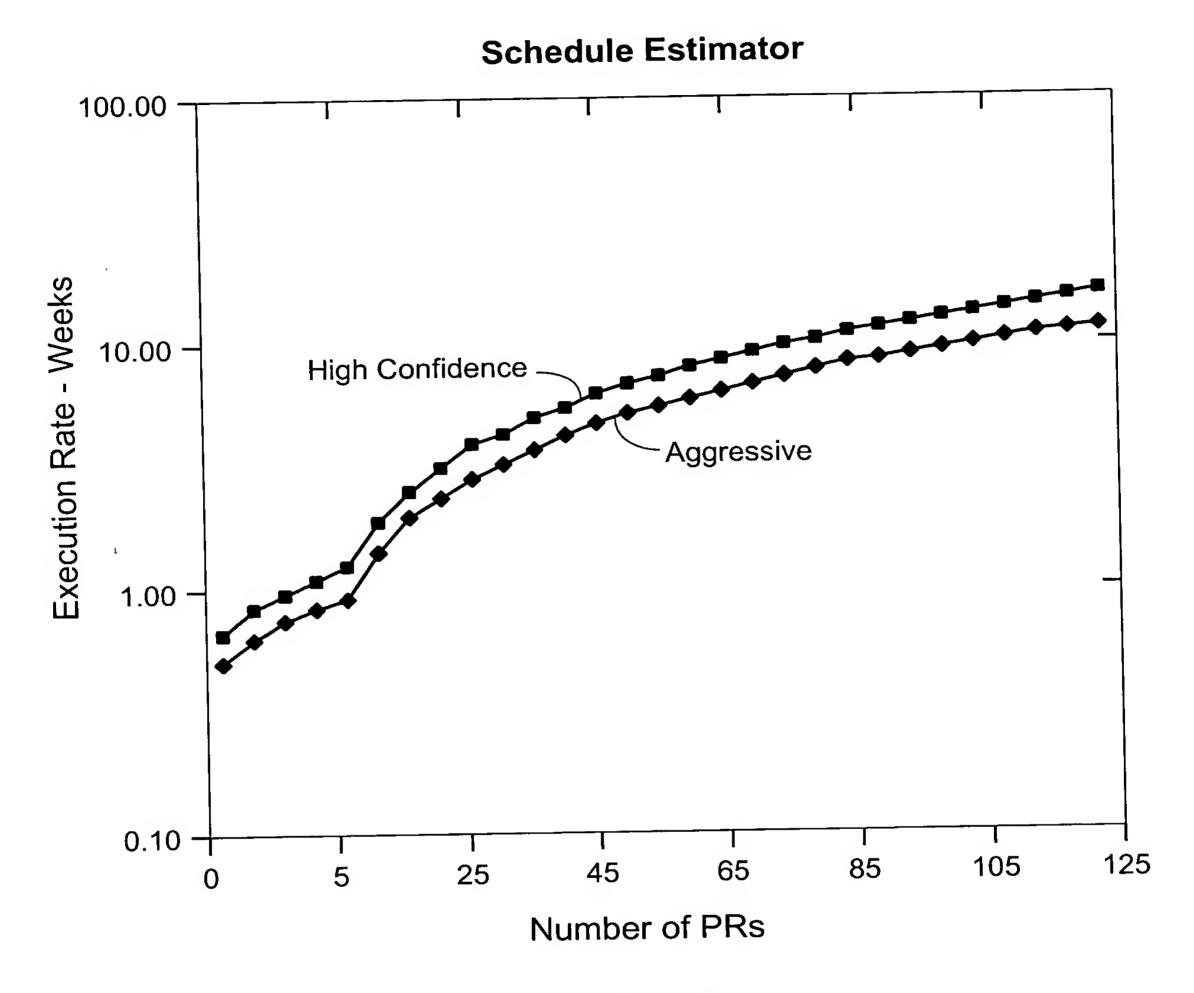

*FIG.*_7
